



CONSTRUCTION UPDATE

WHITNALL
SCHOOL DISTRICT

Hales Corners Elementary
Feb. 18th — Feb. 22nd 2019



CGSCHMIDT INC.

SAFETY:

Please be mindful of the construction area as activities continue. No students, parents, or school staff should pass the fence line without a CG Schmidt escort.

MILESTONE DATES:

- Steel Joists/Decking — February 20th—Goal Achieved
- Roofing Completed — April 2nd
- Enclosure Completed — June 24th

PROGRESS THIS WEEK:

New Addition

- Masonry walls are fully completed with the southwest wall finished.
- Structural steel, joists and decking showed up onsite on time.
- Crane was delivered to site and started swinging steel joists and beams into place, including the student signed beam.

GOAL FOR NEXT WEEK:

New Addition


- Steel joists and beams will continue to be installed.
- The roof deck will be installed using a tool that creates loud noises which will last until 3/6/19. The school, fire dept. and police dept. have been informed.



Masonry Block walls—Fully completed for the new addition



Student Signed Beam Swinging into place

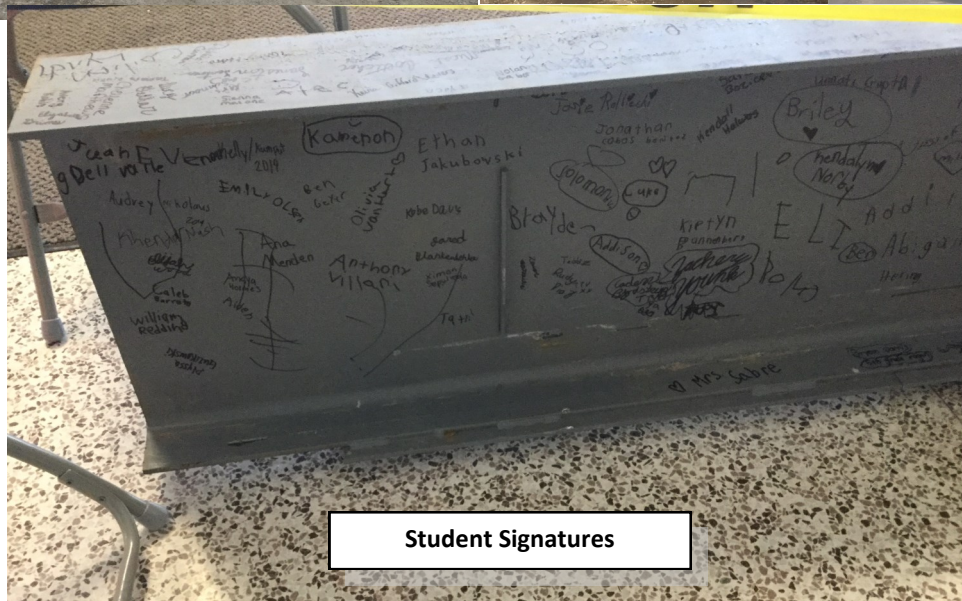

Student Signatures
