



CONSTRUCTION UPDATE

WHITNALL
SCHOOL DISTRICT

Hales Corners Elementary
March 11th—15th 2019



CGSCHMIDT
INC.

SAFETY:

Please be mindful of the construction area as activities continue. No students, parents, or school staff should pass the fence line without a CG Schmidt escort.

PROGRESS THIS WEEK:

New Addition

- The roof blocking is completed.
- Roof Insulation is being put down and rubber roofing set over the top of the insulation.
- The ground thaw system was moved over to the other half of the addition to remove the frost in the ground.
- Temporary heating units are onsite to condition the working space.
- In ground plumbing and electrical work is ongoing before the Slab on Grade is poured over spring break

MILESTONE DATES:

- Roofing Completed — April 2nd
- Enclosure Completed — June 24th


GOAL FOR NEXT WEEK:

New Addition

- Roofing will be completed
- Electrical and plumbing in ground piping will be going in on the east side.
- The subgrade will be leveled off for anticipation of the slab on grade pour.
- Window blocking will be started



Rubber Roofing

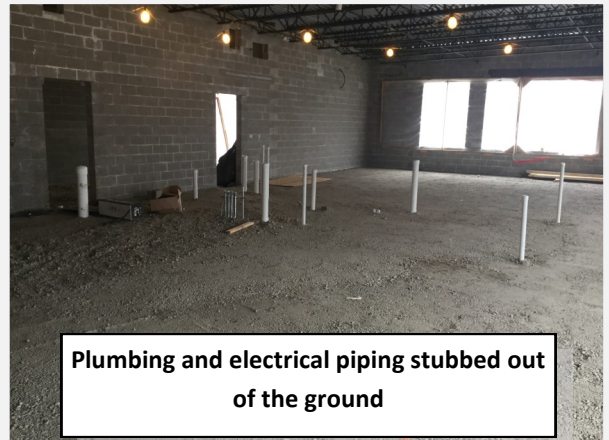

Plumbing and electrical piping stubbed out of the ground



Roof Insulation Sloping to drains
