



CONSTRUCTION UPDATE

WHITNALL
SCHOOL DISTRICT

Whitnall High School
April 8th—26th 2019



SAFETY:

Please be mindful of the construction area as activities continue. No students, parents, or school staff should enter the temporary partitions without a CG Schmidt escort.

PROGRESS:

STEM Wing

- Metal stud walls are up along with door and interior window frames.
- Mechanical, Electrical and Plumbing (MEP) rough in for in wall are being completed soon.
- MEP rough in for above the ceiling are ongoing.
- Exterior storefront glass system is starting to be removed in order to replace with new system.

Auditorium Bathrooms

- All underground plumbing rough ins are complete and concrete is poured.
- Metal studs are up for Electrical, Plumbing, and wood blocking in wall rough ins.

MILESTONE DATES:

- Auditorium bathrooms completed by 6/14/19
- STEM Wing Storefront glass replacement started on 4/29/19

GOAL FOR NEXT UPDATE:

STEM Wing


- MEP In wall is complete
- MEP above ceiling is complete.
- Exterior storefront system will be removed complete and framed in. Will work on getting glass installed complete to make STEM wing dry from outside.

Auditorium Bathrooms

- Complete all in wall rough ins.
- Complete tile backer board and begin setting tile on floors and walls.



Lots of electrical rough in required for all outlets and data needed to support the new STEM classrooms

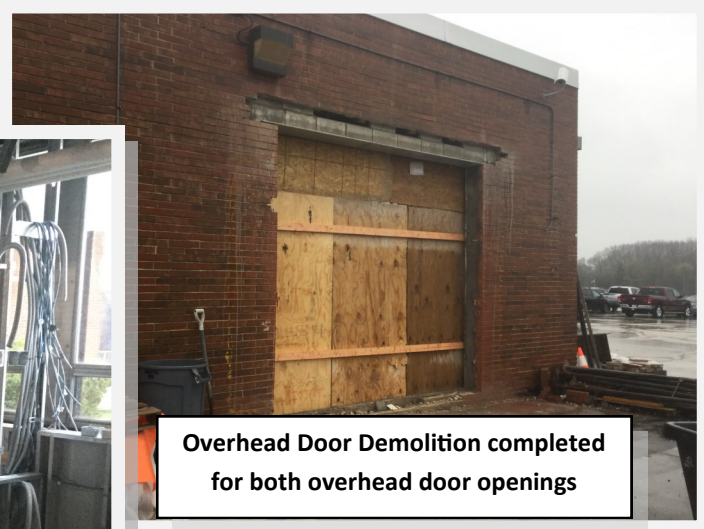

Overhead Door Demolition completed for both overhead door openings



Storefront Glass System is being removed and temporary partitions going up in its place until framing and glass are installed
