



CONSTRUCTION UPDATE

WHITNALL
SCHOOL DISTRICT

Whitnall High School
June 10th—28th 2019



SAFETY:

Please be mindful of the construction area as activities continue. No students, parents, or school staff should enter the temporary partitions without a CG Schmidt escort.

MILESTONE DATES:

- Auditorium bathrooms completed by 6/14/19— Completed!!
- Ceramic Tile started by 7/18/19

PROGRESS:

STEM Wing

- Electrical trim and devices are installed.
- Casework has been Installed.
- Overhead Doors are installed

Auditorium Bathrooms

- Toilet Accessories and doors/hardware have been installed.

Gym Bathrooms

- Demolition is completed.
- The plumbing trench infill has been completed.
- Patching of masonry walls has begun.


GOAL FOR NEXT UPDATE:

STEM Wing

- Ceiling tile will be installed.
- Floor preparation and skim coat will have begun.

Gym Bathrooms

- Bathroom interior walls will be framed and wood blocking installed.
- Plumbing in wall rough in will be completed and inspected to close up walls for ceramic tile to begin.

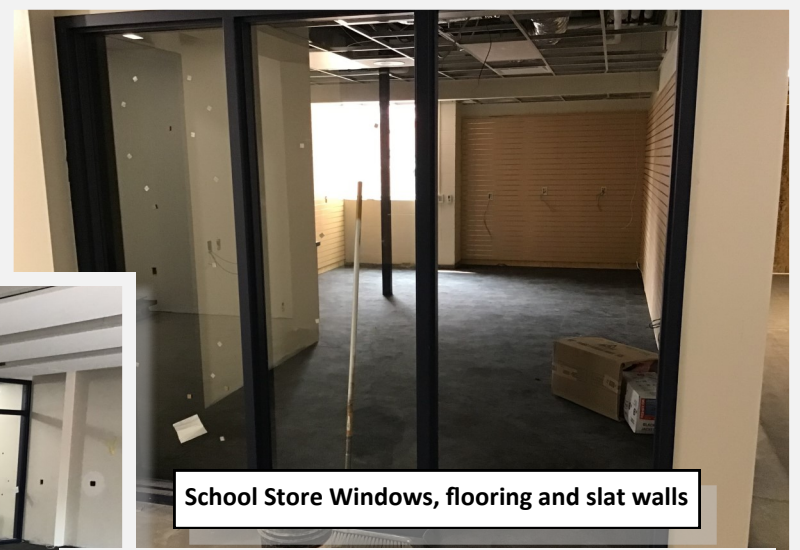

School Store Windows, flooring and slat walls



Business Classroom cabinets and Carpet tile



STEM Corridor Acoustical Ceiling Panel
