



CONSTRUCTION UPDATE

WHITNALL
SCHOOL DISTRICT

Whitnall High School
July 22nd—August 9th 2019



SAFETY:

Please be mindful of the construction area as activities continue. No students, parents, or school staff should enter the temporary partitions without a CG Schmidt escort.

MILESTONE DATES:

- Complete STEM Wing and Turn over to owner for final cleaning and move in—8/5/19—Completed!!
- Complete Gym bathroom and turn over to owner by 8/16

PROGRESS:

STEM Wing

- Final coat of Paint completed
- Flooring and Base Complete.
- Door Hardware Installed
- Punchlist Completed

Gym Bathrooms

- Ceramic Tile has been installed
- Bathroom fixtures are 50% complete

GOAL FOR NEXT UPDATE:

STEM Wing

- Punchlist Completed and area turned over to the owner.

Gym Bathrooms


- Bathroom fixtures will be 100% complete
- Punchlist will be complete.



STEM Classroom



Gym Bathroom Tile and Fixtures

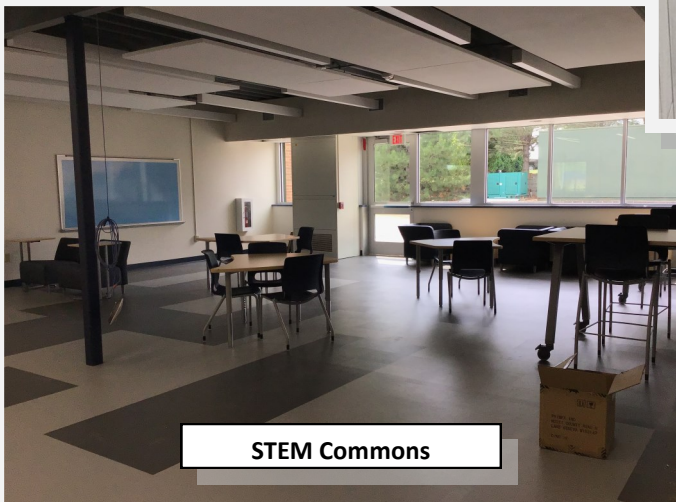

STEM Commons
